



SiteLink

FIELD TO SCHEDULE

Prototype demo walkthrough

Turning unstructured site updates into trusted, schedule-linked progress records

v4 concept prototype | SIH26122


05 October 2026

What this demo covers

17 screens, following the path from field update to approved schedule change.

01	Secure sign-in Access	3	10	Plans & baselines Schedule	12
02	Project overview Home	4	11	Project areas Schedule	13
03	AI Time Agent Capture	5	12	Execution intelligence Intelligence	14
04	Today & work log Capture	6	13	Ask SiteLink SiteLink AI	15
05	Report inbox Review	7	14	Execution memory SiteLink AI	16
06	Conflict center Review	8	15	Progress insights SiteLink AI	17
07	Missing progress updates Review	9	16	Audit trail Governance	18
08	Risks & issues Controls	10	17	Users & roles Governance	19
09	Activity register Schedule	11			

Secure sign-in

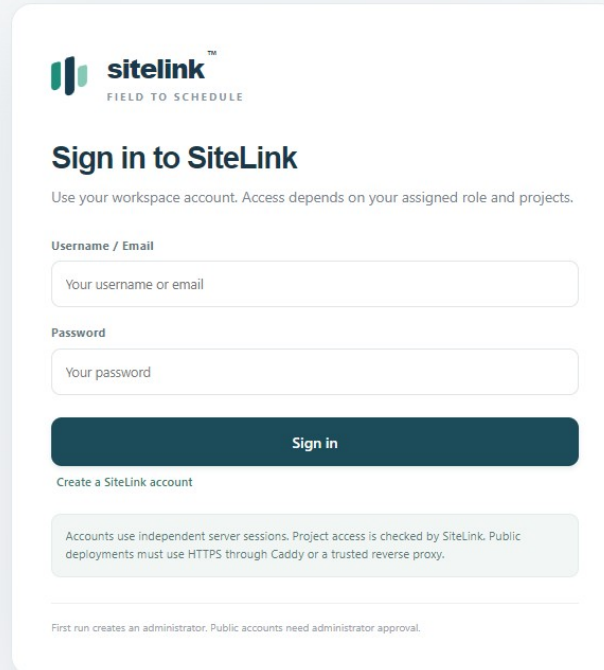

The image shows a sign-in form for SiteLink. At the top is the SiteLink logo with the tagline 'FIELD TO SCHEDULE'. Below the logo is the heading 'Sign in to SiteLink' followed by a subtext: 'Use your workspace account. Access depends on your assigned role and projects.' The form contains two input fields: 'Username / Email' with the placeholder 'Your username or email' and 'Password' with the placeholder 'Your password'. Below these fields is a dark blue 'Sign in' button. Under the button is a link 'Create a SiteLink account'. At the bottom of the form is a light green box containing the text: 'Accounts use independent server sessions. Project access is checked by SiteLink. Public deployments must use HTTPS through Caddy or a trusted reverse proxy.' Below this box is a small line of text: 'First run creates an administrator. Public accounts need administrator approval.'

sitelink™
FIELD TO SCHEDULE

Sign in to SiteLink

Use your workspace account. Access depends on your assigned role and projects.

Username / Email

Password

Sign in

[Create a SiteLink account](#)

Accounts use independent server sessions. Project access is checked by SiteLink. Public deployments must use HTTPS through Caddy or a trusted reverse proxy.

First run creates an administrator. Public accounts need administrator approval.

Role-based workspace login. Access depends on the assigned role and project; the first run creates the administrator and public sign-ups need admin approval.

Why it matters: Field data is visible only to the right people.

Project overview

The screenshot shows the SiteLink project overview dashboard. The left sidebar contains navigation links: HOME, Project overview (active), CAPTURE & REVIEW, Today & work log, Report inbox (6 items), AI Agent, NEEDS ATTENTION, INTELLIGENCE, PROJECT, and SITELINK AI. The main content area is titled 'Project overview' and includes a live view of project progress, field evidence, and decisions. Key metrics include 45.9% weighted actual progress against a 52.4% planned baseline, with a -6.5 point variance. The dashboard also shows today's work, needs attention, and a completion estimate.

SiteLink™
FIELD TO SCHEDULE

PROJECTS / SYNTHETIC PROCESS FACILITY

Shared server · refreshes every 10s | 05 Oct 2026

Ask SiteLink

Synthetic Process Facility
Demo Infrastructure Group · Phase 02

Project overview
A live view of project progress, field evidence, decisions, and what needs attention.

Export data | Log an update

CURRENT PROJECT
Synthetic Process Facility
Phase 02

Ask SiteLink

Project health
Delayed work needs attention

4 activities flagged

45.9% weighted actual progress

Planned 52.4% -6.5 points vs planned

Calculated from 12 activities using Planned duration fallback.

Approved baseline
Version 1
2026-10-05T16:05:26Z · 12 activities

Completion estimate
Not estimated
Insufficient approved history for a completion estimate

Today's work
2026-10-05 · activities in their planned date window

Open work log

PIP-L6-044 · Perform NDT on Line 24-XX welds
Piping · 0% in the schedule

Details Ask SiteLink

Needs attention
Current schedule conditions and open project records

Open attention

Delayed · CIV-L6-014
Complete foundation concrete pour - Rack B4
Planned finish date has passed with work incomplete.
78% actual · 100% planned

Details Ask AI

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

mukesh
Admin

Live project health: 45.9% weighted actual progress against 52.4% planned (-6.5 pts), the approved baseline, today's work and the activities that need attention.

Why it matters: A manager sees what is slipping in one glance.

AI Time Agent

SiteLink™
FIELD TO SCHEDULE

PROJECTS / SYNTHETIC PROCESS FACILITY

Shared server · refreshes every 10s | 05 Oct 2026 | Ask SiteLink

Synthetic Process Facility
Demo Infrastructure Group · Phase 02

HOME

- Project overview

CAPTURE & REVIEW

- Today & work log
- Report inbox (6)
- AI Agent** (AI)

NEEDS ATTENTION

INTELLIGENCE

PROJECT

SITELINK AI

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

mukesh Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet. Server address: <http://127.0.0.1:8000>

FIELD CAPTURE — SUPERVISOR TIME AGENT

AI Time Agent

Describe what happened in ordinary language. Review the extracted facts and ranked schedule links before saving.

Tell the Time Agent what happened
LLM-assisted extraction when configured; local evidence-first fallback when unavailable. Admin

Supervisor update

Example: Line 24 spool erection started at 8:30 this morning in Unit B. Four spools are installed; progress is about 65%.

Auto-detect discipline Location (optional) Report received date 05-10-2026

Confirmed event date dd-mm-yyyy Confirmed progress % Optional Scan diary / photo

Dictate update Analyze update

Scan text for review, or dictate/type an update. Enter a confirmed event date and progress separately if they are not in the source. Voice dictation uses the browser's optional speech recognition. Audio is not saved by SiteLink. Check the transcript before analysis. Scores are heuristic rankings, not calibrated probabilities.

Safe capture flow

- 1 State activity, location, and event clearly.
- 2 Review extracted dates, times, progress, and evidence.
- 3 Choose a candidate only when it is the right schedule node.
- 4 Save to the inbox. A Planner approves or corrects the match.

No activity ID or date is fabricated. Missing details stay blank and uncertain links stay unmatched.

A supervisor describes the day in ordinary language, dictates it or scans a diary photo. SiteLink extracts the facts and ranks schedule links before anything is saved. No activity ID or date is invented; uncertain links stay unmatched.

Why it matters: Field language goes straight into the schedule without manual re-entry.

Today & work log



SP Synthetic Process Facility
Demo Infrastructure Group - Phase 02

HOME

Project overview

CAPTURE & REVIEW

Today & work log

Report inbox 6

AI Agent AI

NEEDS ATTENTION

Risks & issues

Conflict center 1

Missing updates 7

ROLE-PROTECTED WORKSPACE
Server sessions - project access checked

mukesh Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet.

Server address: http://127.0.0.1:8000

FIELD EXECUTION

Today & work log

Submit evidence from site. Planner approval is required before actuals change.

Export data Log an update

Today · 2026-10-05

1 Planned today

0 Updates received

0 Approved

7 Cadence gaps

Supervisor work entry

Supervisor daily work entry

Schedule activity	Work / event date
Select an activity	dd-mm-yyyy
Event type	Event time, if known
Progress update	--:-- --
Progress %	Completed quantity
People on task	Condition
Materials	Equipment used

Progress method

45.9% weighted progress

Planned duration fallback

From 12 activities. Submitted work has no schedule effect until approved.

Recent work history

No submitted updates yet.

Structured daily work entry: activity, event type, progress %, quantity, crew, condition, materials and equipment. Submitted work has no schedule effect until a Planner approves it.

Why it matters: Every number that changes the plan has a reviewer behind it.

Report inbox



Synthetic Process Facility
Demo Infrastructure Group · Phase 02

HOME

Project overview

CAPTURE & REVIEW

Today & work log

Report inbox 6

AI Agent AI

NEEDS ATTENTION

Risks & issues

Conflict center 1

Missing updates 7

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

mukesh Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet.

Server address: <http://127.0.0.1:8000>

SITE UPDATES — PLANNER REVIEW

Report inbox

Turn unstructured updates into trusted, schedule-linked progress records.

↓ Export data + Log an update

Incoming progress reports Remove sample reports + Import reports

One queue for reports from every discipline
Text, CSV, and XLSX reports are parsed, then linked to the activity register. 6 awaiting planner review

Search reports Source, report text, ID, reviewer


All reports 6 Needs review 6 Unmatched 0 Reviewed 0 Removed 0

sample-data/progress_updates.csv DEFAULT SAMPLE RPT-SAMPLE-01 Piping team erected four spools on Line 24-XX in Unit 8 today. The activity is around 65% complete; fit-up checks continue on the north side. R. Das - Site supervisor - Added by Sample data - 29 Sept 26	PIP-L6-042 · Erect Line 24-XX pipe spools Piping · 69% heuristic match Needs review Review Remove
sample-data/progress_updates.csv DEFAULT SAMPLE RPT-SAMPLE-02 Cable tray installation at Substation A finished today. Inspection passed; close the activity. M. Nair - Electrical lead - Added by Sample data - 29 Sept 26	ELE-L5-019 · Install cable tray in Substation A Electrical · 72% heuristic match Needs review Review Remove
sample-data/progress_updates.csv DEFAULT SAMPLE RPT-SAMPLE-03 Started calibration of PT-220 pressure transmitter in Process Train 2. Initial loop check is complete. S. Roy - Instrument lead - Added by Sample data - 29 Sept 26	INS-L6-008 · Calibrate pressure transmitter PT-220 Instrumentation · 82% heuristic match Needs review Review Remove
sample-data/progress_updates.csv DEFAULT SAMPLE RPT-SAMPLE-05 Contractor daily report: Line 24-XX pipe installation is 80% complete. Crew waiting on carbon-steel fittings from stores. ABC Piping contractor - Added by Sample data - 29 Sept 26	PIP-L6-042 · Erect Line 24-XX pipe spools Piping · 59% heuristic match Needs review Review Remove

One queue for text, CSV and XLSX reports from every discipline. Each report is linked to a suggested L5/L6 activity with a heuristic match score; the Planner reviews or removes it. 6 reports await review.

Why it matters: Unstructured site updates become trusted, schedule-linked records.

Conflict center

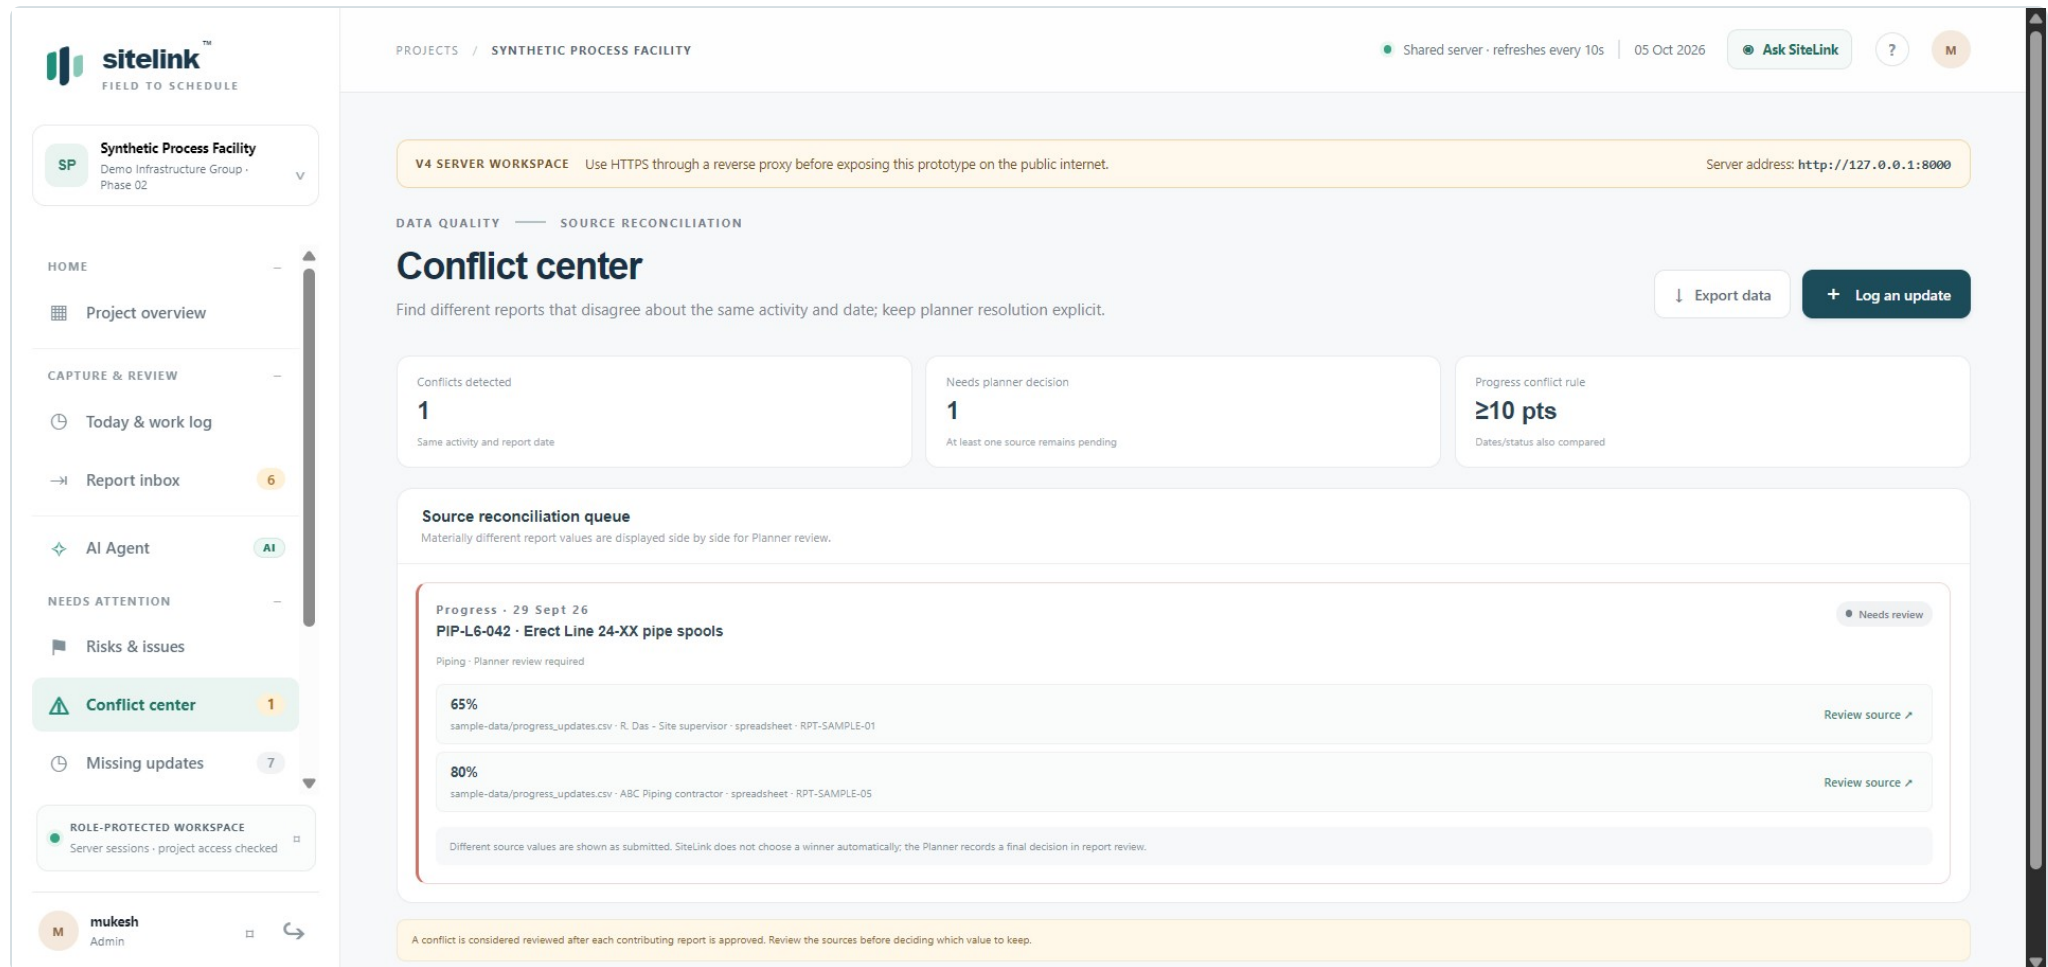

SiteLink™
FIELD TO SCHEDULE

PROJECTS / SYNTHETIC PROCESS FACILITY

Shared server · refreshes every 10s | 05 Oct 2026 | [Ask SiteLink](#) | ? | M

Synthetic Process Facility
Demo Infrastructure Group · Phase 02

HOME

- Project overview

CAPTURE & REVIEW

- Today & work log
- Report inbox (6)

AI Agent (AI)

NEEDS ATTENTION

- Risks & issues
- Conflict center (1)**
- Missing updates (7)

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

M mukesh Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet. Server address: <http://127.0.0.1:8000>

DATA QUALITY — SOURCE RECONCILIATION

Conflict center

Find different reports that disagree about the same activity and date; keep planner resolution explicit.

↓ Export data + Log an update

Conflicts detected
1
Same activity and report date

Needs planner decision
1
At least one source remains pending

Progress conflict rule
≥10 pts
Dates/status also compared

Source reconciliation queue
Materially different report values are displayed side by side for Planner review.

Progress · 29 Sept 26
PIP-L6-042 · Erect Line 24-XX pipe spools
Piping · Planner review required

65%
sample-data/progress_updates.csv · R. Das · Site supervisor · spreadsheet · RPT-SAMPLE-01

Review source ↗

80%
sample-data/progress_updates.csv · ABC Piping contractor · spreadsheet · RPT-SAMPLE-05

Review source ↗

Different source values are shown as submitted. SiteLink does not choose a winner automatically; the Planner records a final decision in report review.

A conflict is considered reviewed after each contributing report is approved. Review the sources before deciding which value to keep.

Flags reports that disagree about the same activity and date. Here two sources report 65% and 80% for PIP-L6-042 (rule: difference of 10 pts or more). SiteLink does not pick a winner; the Planner decides.

Why it matters: Disagreements are surfaced and resolved explicitly, not averaged away.

Missing progress updates



FIELD TO SCHEDULE

SP Synthetic Process Facility

Demo Infrastructure Group - Phase 02

HOME

Project overview

CAPTURE & REVIEW

Today & work log

Report inbox 6

AI Agent AI

NEEDS ATTENTION

Risks & issues

Conflict center 1

Missing updates 7

ROLE-PROTECTED WORKSPACE

Server sessions - project access checked

mukesh Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet.

Server address: http://127.0.0.1:8000

DATA COMPLETENESS — UPDATE CADENCE

Missing progress updates

Spot active scheduled activities without a linked update inside their expected reporting window.

Completeness check, not a delay verdict

Open activities are flagged after their reporting cadence elapses. Default cadence is 48 hours; set update_cadence_hours in a schedule CSV to customize it.

Open activities without a recent linked report 7 items

ACTIVITY ID	OWNER / DISCIPLINE	LAST UPDATE	MISSING FOR	EXPECTED CADENCE	SCHEDULE STATE	ACTION
CIV-L6-014	Complete foundation concrete pour - Rack B4 Civil - Civil crew	No report received	11d 0h	48 hours	In progress	Log / review update
PIP-L6-042	Erect Line 24-XX pipe spools Piping - Piping crew 2	No report received	10d 0h	48 hours	In progress	Log / review update
PIP-L6-057	Hydrotest cooling-water header CW-04 Piping - Piping crew 1	No report received	8d 0h	48 hours	At risk	Log / review update
INS-L6-008	Calibrate pressure transmitter PT-220 Instrumentation - Instrument team	No report received	7d 0h	48 hours	In progress	Log / review update
CIV-L6-022	Backfill pipe-rack trench - Zone C Civil - Civil crew	No report received	6d 0h	48 hours	Not started	Log / review update
EQP-L6-003	Align Pump P-103 and verify coupling Equipment - Mechanical team	No report received	6d 0h	48 hours	Not started	Log / review update
PIP-L6-043	Weld Line 24-XX erected spools Piping - Piping welding crew	No report received	4d 0h	48 hours	Not started	Log / review update

Lists open activities with no linked report inside the 48-hour cadence window, showing days missing, schedule state and a quick log action. 7 activities are flagged.

Why it matters: A completeness check that shows where site visibility has gone dark.

Risks & issues

The screenshot shows the SiteLink interface for the 'SYNTHETIC PROCESS FACILITY' project. The left sidebar contains navigation links: HOME, Project overview, CAPTURE & REVIEW, Today & work log, Report inbox (6), AI Agent (AI), NEEDS ATTENTION, Risks & issues (selected), Conflict center (1), Missing updates (7), and a ROLE-PROTECTED WORKSPACE status. The main content area is titled 'Risks & issues' and includes a sub-header 'PROJECT CONTROLS'. A yellow banner at the top right of the main area states: 'V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet. Server address: http://127.0.0.1:8000'. Below this, the 'Project risk register' section shows 'No project risks or issues are recorded.' To the right, the 'New risk or issue' form is visible, with fields for Title, Severity (Medium), Probability (Medium), Owner, Due date (dd-mm-yyyy), Linked activity (Project-level), Description, and Mitigation. The bottom of the sidebar shows the user 'mukesh Admin'.

Risk register with severity, probability, owner, due date, linked activity, description and mitigation, tracked against the schedule.

Why it matters: Risks are tied to activities instead of living in a separate spreadsheet.

Activity register



FIELD TO SCHEDULE

SP Synthetic Process Facility
Demo Infrastructure Group - Phase 02

NEEDS ATTENTION

- Risks & issues
- Conflict center 1
- Missing updates 7

INTELLIGENCE

- Execution analysis

PROJECT

- Activity register 12**
- Plans & baselines
- Project areas

ROLE-PROTECTED WORKSPACE

Server sessions - project access checked

mukesh
Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet.

Server address: <http://127.0.0.1:8000>

PLANNING TO EXECUTION — ACTIVITY REGISTER

Activity register

Review L5/L6 work items alongside the latest actual progress captured from site.

Export data Log an update

Baseline schedule and actuals
Every change is linked back to its field source and reviewer.

Search activity, ID, location Import CSV / XLSX / MS Project XML

All activities 12 Open 9 Complete 3 Overdue 7

ACTIVITY ID	ACTIVITY	DISCIPLINE	PLANNED DATES	ACTUAL DATES	PROGRESS	VARIANCE	STATUS	UPDATES
CIV-L6-014 WBS 1.2.4.1	Complete foundation concrete pour - Rack B4 Unit B - Grid B4 - Civil crew	Civil	24 Sept 26 to 27 Sept 26 - 4 calendar days	25 Sept 26 to — - actual — days	78%	-22 pts	In progress	0 updates
CIV-L6-022 WBS 1.4.2.2	Backfill pipe-rack trench - Zone C Zone C - Pipe rack - Civil crew	Civil	29 Sept 26 to 03 Oct 26 - 5 calendar days	— to — - actual — days	0%	-10 pts	Not started	0 updates
ELE-L5-019 WBS 3.1.5.2	Install cable tray in Substation A Substation A - Electrical team	Electrical	22 Sept 26 to 26 Sept 26 - 5 calendar days	22 Sept 26 to 28 Sept 26 - actual 7 days - +2d vs plan	100%	On plan	Complete	0 updates
EQP-L6-003 WBS 5.1.1.3	Align Pump P-103 and verify coupling Pump House - P-103 - Mechanical team	Equipment	29 Sept 26 to 02 Oct 26 - 4 calendar days	— to — - actual — days	0%	-15 pts	Not started	0 updates
HSE-L5-006 WBS 6.2.1.4	Complete confined-space permit inspection Tank T-08 - HSE shift A	HSE	25 Sept 26 to 27 Sept 26 - 3 calendar days	25 Sept 26 to 27 Sept 26 - actual 3 days - 0d vs plan	100%	On plan	Complete	0 updates
INS-L6-008 WBS 4.3.2.8	Calibrate pressure transmitter PT-220 Process Train 2 - Instrument team	Instrumentation	28 Sept 26 to 30 Sept 26 - 3 calendar days	29 Sept 26 to — - actual — days	45%	-5 pts	In progress	0 updates
PIP-L6-040 WBS 2.4.1.4	Erect Line 23-XX pipe spools Unit B - Line 23-XX - Piping crew 1	Piping	20 Aug 26 to 22 Aug 26 - 3 calendar days	20 Aug 26 to 24 Aug 26 - actual 5 days - +2d vs plan	100%	On plan	Complete	0 updates
PIP-L6-042 WBS 2.4.1.6	Erect Line 24-XX pipe spools Unit B - Line 24-XX - Piping crew 2	Piping	25 Sept 26 to 30 Sept 26 - 6 calendar days	26 Sept 26 to — - actual — days	65%	-2 pts	In progress	0 updates

Baseline L5/L6 work items alongside the latest actuals: planned vs actual dates, progress, variance, status and update count. Schedules can be imported from CSV, XLSX or MS Project XML.

Why it matters: Plan and field reality sit side by side, each change traceable to its source.

Plans & baselines

SiteLink™
FIELD TO SCHEDULE

PROJECTS / SYNTHETIC PROCESS FACILITY

Shared server · refreshes every 10s | 05 Oct 2026 | Ask SiteLink | ? | M

Synthetic Process Facility
Demo Infrastructure Group · Phase 02

NEEDS ATTENTION

- Risks & issues
- Conflict center 1
- Missing updates 7

INTELLIGENCE

- Execution analysis

PROJECT

- Activity register 12
- Plans & baselines**
- Project areas

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

M mukesh
Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet. Server address: `http://127.0.0.1:8000`

PLANNING

Plans & baselines

Review plan versions before changing the working schedule.

Plan versions

Working activities: 12

Only approved baseline versions replace planned schedule fields.

+ Upload plan version

No plan versions uploaded.

Approved baseline history

Baseline v1

Approved 2026-10-05T16:05:26Z · 12 activities

Approved

Current progress

45.9%

Planned duration fallback

12 activities contribute.

SITELINK · SIH26122 v4 concept prototype

Workspace records stay in the configured server database

Plan versions are reviewed before they change the working schedule. Only an approved baseline replaces planned fields; Baseline v1 (12 activities) is approved and current progress is shown.

Why it matters: The baseline cannot be overwritten by accident.

Project areas

Sitelink™
FIELD TO SCHEDULE

PROJECTS / SYNTHETIC PROCESS FACILITY

Shared server · refreshes every 10s | 05 Oct 2026 | Ask SiteLink | ? | M

Synthetic Process Facility
Demo Infrastructure Group · Phase 02

NEEDS ATTENTION

- Risks & issues
- Conflict center 1
- Missing updates 7

INTELLIGENCE

- Execution analysis

PROJECT

- Activity register 12
- Plans & baselines
- Project areas**

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

mukesh
Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet. Server address: `http://127.0.0.1:8000`

PROJECT STRUCTURE

Project areas

Organize activities by work area and sub-area.

Area hierarchy

No areas are defined yet.

Manage hierarchy

Add to project hierarchy

Type: Area | Parent area: Choose for sub-area

Name:

Decision reason (required):

Add area

SITELINK · SIH26122 v4 concept prototype

Workspace records stay in the configured server database

Organise activities into work areas and sub-areas. Every hierarchy change requires a decision reason.

Why it matters: Progress and delays can be viewed by physical area, with a reason on record.

Execution intelligence



Synthetic Process Facility
Demo Infrastructure Group · Phase 02

Report inbox 6

AI Agent AI

NEEDS ATTENTION -

Risks & issues

Conflict center 1

Missing updates 7

INTELLIGENCE -

Execution analysis

PROJECT +

SITELINK AI +

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

mukesh Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet. Server address: <http://127.0.0.1:8000>

EXECUTION INTELLIGENCE

Execution intelligence

Trace approved field evidence through causes, dependency effects, forecasts, human decisions, and recorded outcomes.

Export data Log an update

Judge walkthrough data
Load a clearly marked synthetic material-delay story with linked evidence, a predecessor chain, a milestone, and reviewed progress. Load synthetic story

Approved updates
0

Open causes
0

Downstream activities
0

Forecast source records
0

Schedule structure
CPM, dependencies, and critical path

Area and sub-area execution

Process Train 2
Sub-area not recorded 1 activities

Approved updates
0

Linked causes
0

Impacted activities
0

Latest approved update: None recorded · Source records:
Activity IDs: INS-L6-008

Pump House - P-103
Sub-area not recorded 1 activities

Project execution thread

Events link the activity, source record, supporting evidence, and human decision. Synthetic sample records are labeled.

baseline · 2026-10-05T16:05:26Z
Planner-approved baseline version 1 (12 activities)
Project record · Area not recorded · Sub-area not recorded · baseline-67b24c359513

Method and boundaries

Deterministic rules over stored schedule and planner-approved execution records; causal labels and forecasts need human review and never change schedule actuals.

- Dependency links come from saved schedule predecessors.

Traces approved field evidence through causes, dependency effects, forecasts and human decisions, using CPM, dependencies and the critical path. Rules are deterministic and never change schedule actuals. A labelled synthetic story can be loaded for walkthroughs.

Why it matters: Shows why a delay matters downstream, not just that it happened.

Ask SiteLink

Sitelink™
FIELD TO SCHEDULE

PROJECTS / SYNTHETIC PROCESS FACILITY

Shared server · refreshes every 10s | 05 Oct 2026

Ask SiteLink

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet. Server address: <http://127.0.0.1:8000>

EXECUTION INTELLIGENCE — EVIDENCE-LED Q&A

Ask SiteLink

Investigate project execution with scoped schedule calculations and reviewed evidence.

Export data Log an update

Ask SiteLink about this project
Answers use this project's schedule calculations and reviewed source records. Ask about a specific activity or investigate an area. Read only

Your question

Why is PIP-L6-042 behind, and which approved records support the answer?

Activity scope **Area investigation (optional)**

Whole project No area filter Ask SiteLink

Recorded blockers Critical path Execution history

AI explanations are optional and server configured. Heuristic intent labels are not calibrated. A source document cannot issue instructions to the assistant. SiteLink will label missing facts and will not approve work or change the schedule.

0 project area(s) available. Answers are read-only.

SITELINK · SIH26122 v4 concept prototype

Workspace records stay in the configured server database

Evidence-led, read-only Q&A scoped to the whole project, an activity or an area, for example 'Why is PIP-L6-042 behind, and which approved records support the answer?'. Source documents cannot instruct the assistant, and missing facts are labelled.

Why it matters: Answers cite reviewed evidence instead of guessing.

Execution memory

SiteLink™
FIELD TO SCHEDULE

PROJECTS / SYNTHETIC PROCESS FACILITY

Shared server · refreshes every 10s | 05 Oct 2026

Ask SiteLink ? M

Synthetic Process Facility
Demo Infrastructure Group · Phase 02

Execution memory

PROJECT

- Activity register 12
- Plans & baselines
- Project areas

SITELINK AI

- Ask & investigate
- Execution memory**
- Evidence insights

MORE +

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

M mukesh
Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet. Server address: <http://127.0.0.1:8000>

SITELINK AI — PROJECT MEMORY

Execution memory

Review completed activity history and planner-recorded recovery outcomes for this project.

↓ Export data + Log an update

Completed fingerprints

0

Need planned and actual dates

Average actual duration

—

Small sample observation only

Reported why-chains

0

Based on explicit blocker language

Ask project execution memory
Queries are answered from stored sample fingerprints; no predictive claim is made.

What was the average actual duration?

Ask memory

Ask a question to query the saved execution records.
Current sample data

COMPLETED EXECUTION FINGERPRINTS

No complete fingerprints yet
Approve a report with actual start and finish dates on a completed activity.

REPORTED CAUSE → SCHEDULE-LINKED EXPOSURE

Reviews completed-activity history and planner-recorded recovery outcomes: execution fingerprints, average actual duration and reported why-chains. Answers come from stored records and make no predictive claim.

Why it matters: Lessons from finished work are kept for future planning.

Progress insights

The screenshot shows the SiteLink AI interface for the 'Synthetic Process Facility' project. The left sidebar contains navigation options: 'Synthetic Process Facility' (selected), 'Activity register' (12 items), 'Plans & baselines', 'Project areas', 'Ask & investigate', 'Execution memory', 'Evidence insights' (highlighted), and 'Role-protected workspace'. The main content area is titled 'Progress insights' and includes a description: 'See where actual progress is moving and preserve patterns for future planning.' It features three summary cards: 'Approved reports' (0), 'Approved progress values' (0), and 'Historical duration pairs' (0). Below these are sections for 'Approved progress by discipline' (no data), 'Source-reported blockers' (no blockers), and 'Execution history' (no data). A footer note states: 'History comes from reviewed evidence. Only approved records contribute to execution memory and these summaries. Small synthetic samples do not support statistical predictions.'

SiteLink™
FIELD TO SCHEDULE

PROJECTS / SYNTHETIC PROCESS FACILITY

Shared server · refreshes every 10s | 05 Oct 2026 | Ask SiteLink

Synthetic Process Facility
Demo Infrastructure Group · Phase 02

EXECUTION LEARNING — PROJECT INSIGHTS

Progress insights

See where actual progress is moving and preserve patterns for future planning.

Export data | Log an update

Approved reports
0
Reviewed source records

Approved progress values
0
Records behind progress insight

Historical duration pairs
0
Complete approved executions

Approved progress by discipline
Average progress stated in approved reports. Each group shows its source record count.
No approved progress values are available yet.

Source-reported blockers
These are reported observations, not verified root causes or forecasts.
No approved report contains an explicit blocker.

Execution history
Historical observations from completed activity records; not a forecast.
No completed activity has both planned and actual dates linked to an approved report.

History comes from reviewed evidence
Only approved records contribute to execution memory and these summaries. Small synthetic samples do not support statistical predictions.

ROLE-PROTECTED WORKSPACE
Server sessions · project access checked

mukesh
Admin

Approved progress by discipline, source-reported blockers and execution history. Only approved, reviewed records contribute.

Why it matters: Patterns come from verified evidence, not raw reports.

Audit trail



SP Synthetic Process Facility

Demo Infrastructure Group - Phase 02

Plans & baselines
Project areas
SITELINK AI
Ask & investigate
Execution memory
Evidence insights
MORE
Audit trail
Users & roles
ROLE-PROTECTED WORKSPACE
Server sessions - project access checked
mukesh Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet.

Server address: http://127.0.0.1:8000

DATA GOVERNANCE — CHANGE HISTORY

Audit trail

See who changed each record, when, from which source, what changed, and why.

Export data
Log an update

Who changed what, when, where, and why
Server-recorded history for report additions, reviews, removals, and access changes. Expand a record to see its before and after details.
Export audit CSV

WHEN (UTC)	WHO / ROLE	WHAT CHANGED	WHERE / SOURCE	WHY
2026-10-05 16:05:47Z	M mukesh Admin	Account: (mukesh) - role Admin Created first administrator View record details	First-run setup Device IP 127.0.0.1 WORKSPACE	Workspace owner account created.
2026-10-05 16:05:26Z	SD System demo System	Pipe spool erection on Line 23-XX completed at 100% on 24 Aug 2026. Work was delayed by material availability; delivery came late. Added default sample report View record details	sample-data/progress_updates.csv RPT-SAMPLE-06	Seeded synthetic example so the prototype opens with demo data.
2026-10-05 16:05:26Z	SD System demo System	Contractor daily report: Line 24-XX pipe installation is 80% complete. Crew waiting on carbon-steel fittings from stores. Added default sample report View record details	sample-data/progress_updates.csv RPT-SAMPLE-05	Seeded synthetic example so the prototype opens with demo data.
2026-10-05 16:05:26Z	SD System demo System	Backfill activity in Zone C cannot start until the buried utility clearance is signed. Crew reassigned to north access road. Added default sample report View record details	sample-data/progress_updates.csv RPT-SAMPLE-04	Seeded synthetic example so the prototype opens with demo data.
2026-10-05 16:05:26Z	SD System demo System	Started calibration of PT-220 pressure transmitter in Process Train 2. Initial loop check is complete. Added default sample report View record details	sample-data/progress_updates.csv RPT-SAMPLE-03	Seeded synthetic example so the prototype opens with demo data.
2026-10-05 16:05:26Z	SD System demo System	Cable tray installation at Substation A finished today. Inspection passed; close the activity. Added default sample report View record details	sample-data/progress_updates.csv RPT-SAMPLE-02	Seeded synthetic example so the prototype opens with demo data.

Server-recorded history of who changed what, when, from which source and why, with before/after detail per record and a CSV export.

Why it matters: Full accountability for every record, addition, review and removal.

Users & roles



FIELD TO SCHEDULE

Synthetic Process Facility
Demo Infrastructure Group - Phase 02

Plans & baselines

Project areas

SITELINK AI

Ask & investigate

Execution memory

Evidence insights

MORE

Audit trail

Users & roles

ROLE-PROTECTED WORKSPACE
Server sessions - project access checked

mukesh
Admin

V4 SERVER WORKSPACE Use HTTPS through a reverse proxy before exposing this prototype on the public internet.

Server address: <http://127.0.0.1:8000>

ACCESS CONTROL — WORKSPACE ADMINISTRATION

Users & roles

Create workspace accounts and assign the least access each teammate needs.

↓ Export data + Log an update

Pending Users

Self-registered accounts start as Viewers and receive no project access until approved and assigned.

0 pending

No accounts are waiting for approval.

Workspace accounts

Each teammate has an independent session. Access is scoped to assigned projects and enforced by the server.

+ Add user

ACCOUNT	ROLE	PROJECT ACCESS / STATE	CREATED	LAST LOGIN	ADMIN ACTIONS
 mukesh mukesh	Admin	All workspace projects Active	05 Oct 26	2026-10-05 16:05:47Z	Edit · Reset password · Disable

1 account

Role, access, password, and project changes are audited

Projects and memberships

Projects are isolated. Add a member to grant access, then adjust the member's role permissions.

+ Create project

Synthetic Process Facility

Demo Infrastructure Group - Phase 02

1 project

Admins can access all projects in this workspace

Admin

Manage workspace users, projects, memberships, and audit history.

Planner

Review and approve matches only in assigned projects and with granted permissions.

Admin approval for self-registered accounts, per-user sessions, role assignment (Admin, Planner and more) and project memberships. Access is least-privilege and enforced by the server.

Why it matters: Each teammate sees only the projects and actions they need.
